


🏠 CONSENTINO MIDDLE SCHOOL			788	29-Mar-24 08:00 A	30-Apr-27 16:00	0											3
📁 COMMENCEMENT			692	29-Mar-24 08:00 A	30-Apr-27 16:00	0											3
📁 MILESTONES			692	29-Mar-24 08:00 A	30-Apr-27 16:00	0											3
📄 01000.00	NOTICE TO PROCEED	0	29-Mar-24 08:00 A			0	▶ NOTICE TO PROCEED, 29-Mar-24 08:00 A										
📄 17500.01	PHASE 1 COMPLETION	0		18-Mar-26 16:00		0	◆ PHASE 1 COMPLETION,										
📄 17500.02	PHASE 2 COMPLETION	0		14-Aug-26 16:00		0	◆ PHASE 2 COMPLETION,										
📄 17500.03	PHASE 3 COMPLETION	0		30-Apr-27 16:00		0	◆ P										
📁 SUBMITTALS & PROCUREMENT			365	29-Mar-24 08:00 A	23-Sep-25 17:00	228	▼ 23-Sep-25 17:00, SUBMITTALS & PROCUREMENT										
📁 PREPARE/SUBMIT			192	29-Mar-24 08:00 A	30-Dec-24 17:00	405	▶ 30-Dec-24 17:00, PREPARE/SUBMIT										
📄 03300-A	PREPARE/SUBMIT - REBAR SHOP DRAWINGS/CONC. MIX DESIGNS / AB's	10	29-Mar-24 08:00 A	22-Apr-24 17:00 A			📄	PREPARE/SUBMIT - REBAR SHOP DRAWINGS/CONC. MIX DESIGNS / AB's									
📄 04200-A	PREPARE/SUBMIT - MASONRY - EXT. BRICK SAMPLES	62	29-Mar-24 08:00 A	27-Jun-24 17:00 A			📄	PREPARE/SUBMIT - MASONRY - EXT. BRICK SAMPLES									
📄 05120-A	PREPARE/SUBMIT - STRUCTURAL STEEL FRAMING - SEQUENCES	15	29-Mar-24 08:00 A	21-Jun-24 17:00 A			📄	PREPARE/SUBMIT - STRUCTURAL STEEL FRAMING - SEQUENCES									
📄 05510-A	PREPARE/SUBMIT - METAL STAIRS/RAILINGS	70	29-Mar-24 08:00 A	23-Jul-24 17:00 A			📄	PREPARE/SUBMIT - METAL STAIRS/RAILINGS									
📄 07210-A	PREPARE/SUBMIT - INSULATION - MINERAL WOOL	40	29-Mar-24 08:00 A	03-May-24 17:00 A			📄	PREPARE/SUBMIT - INSULATION - MINERAL WOOL									
📄 07420-A	PREPARE/SUBMIT - METAL WALL PANELS	40	29-Mar-24 08:00 A	03-May-24 17:00 A			📄	PREPARE/SUBMIT - METAL WALL PANELS									
📄 07500-A	PREPARE/SUBMIT - ROOFING	35	29-Mar-24 08:00 A	04-Jun-24 17:00 A			📄	PREPARE/SUBMIT - ROOFING									
📄 07840-A	PREPARE/SUBMIT - FIREPROOFING	40	29-Mar-24 08:00 A	17-May-24 17:00 A			📄	PREPARE/SUBMIT - FIREPROOFING									
📄 08100-A	PREPARE/SUBMIT - HOLLOW METAL FRAMES	50	29-Mar-24 08:00 A	28-May-24 17:00 A			📄	PREPARE/SUBMIT - HOLLOW METAL FRAMES									
📄 08200-A	PREPARE/SUBMIT - DOORS	50	29-Mar-24 08:00 A	17-May-24 17:00 A			📄	PREPARE/SUBMIT - DOORS									
📄 08430-A	PREPARE/SUBMIT - STOREFRONT/CURTAINWALLS	50	29-Mar-24 08:00 A	21-Jun-24 17:00 A			📄	PREPARE/SUBMIT - STOREFRONT/CURTAINWALLS									
📄 08510-A	PREPARE/SUBMIT - WINDOWS	50	29-Mar-24 08:00 A	21-Jun-24 17:00 A			📄	PREPARE/SUBMIT - WINDOWS									
📄 08710-A	PREPARE/SUBMIT - HARDWARE	50	29-Mar-24 08:00 A	17-May-24 17:00 A			📄	PREPARE/SUBMIT - HARDWARE									
📄 08800-A	PREPARE/SUBMIT - GLAZING	60	29-Mar-24 08:00 A	26-Apr-24 17:00 A			📄	PREPARE/SUBMIT - GLAZING									
📄 09650-A	PREPARE/SUBMIT - FLOORING - CARPET	80	29-Mar-24 08:00 A	25-Jun-24 17:00 A			📄	PREPARE/SUBMIT - FLOORING - CARPET									
📄 10110-A	PREPARE/SUBMIT - VISUAL DISPLAY UNITS - MARKER/TACKBOARD	80	29-Mar-24 08:00 A	12-Jul-24 17:00 A			📄	PREPARE/SUBMIT - VISUAL DISPLAY UNITS - MARKER/TACKBOARD									
📄 10210-A	PREPARE/SUBMIT - TOILET COMPARTMENTS	70	29-Mar-24 08:00 A	10-Jun-24 17:00 A			📄	PREPARE/SUBMIT - TOILET COMPARTMENTS									
📄 10220-A	PREPARE/SUBMIT - FOLDING PANEL PARTITIONS	60	29-Mar-24 08:00 A	29-May-24 17:00 A			📄	PREPARE/SUBMIT - FOLDING PANEL PARTITIONS									
📄 10280-A	PREPARE/SUBMIT - TOILET/BATH ACCESSORIES	70	29-Mar-24 08:00 A	22-May-24 17:00 A			📄	PREPARE/SUBMIT - TOILET/BATH ACCESSORIES									
📄 11400-A	PREPARE/SUBMIT - FOOD SERVICE EQUIPMENT	60	29-Mar-24 08:00 A	01-Jul-24 17:00 A			📄	PREPARE/SUBMIT - FOOD SERVICE EQUIPMENT									
📄 11520-A	PREPARE/SUBMIT - PROJECTION SCREENS	70	29-Mar-24 08:00 A	12-Jul-24 17:00 A			📄	PREPARE/SUBMIT - PROJECTION SCREENS									
📄 12480-A	PREPARE/SUBMIT - ENTRANCE FLOOR MATS & FRAMES	65	29-Mar-24 08:00 A	15-May-24 17:00 A			📄	PREPARE/SUBMIT - ENTRANCE FLOOR MATS & FRAMES									
📄 12660-A	PREPARE/SUBMIT - TELESCOPING BLEACHERS	70	29-Mar-24 08:00 A	29-May-24 17:00 A			📄	PREPARE/SUBMIT - TELESCOPING BLEACHERS									
📄 14210-A	PREPARE/SUBMIT - ELEVATORS	40	29-Mar-24 08:00 A	19-Apr-24 17:00 A			📄	PREPARE/SUBMIT - ELEVATORS									
📄 21310-A	PREPARE/SUBMIT - FIRE SPRINKLER SYSTEM + EQUIPMENT	60	29-Mar-24 08:00 A	12-Jul-24 17:00 A			📄	PREPARE/SUBMIT - FIRE SPRINKLER SYSTEM + EQUIPMENT									
📄 22100-A	PREPARE/SUBMIT - PLUMBING MATERIALS + ACCESSORIES	15	29-Mar-24 08:00 A	20-Jun-24 17:00 A			📄	PREPARE/SUBMIT - PLUMBING MATERIALS + ACCESSORIES									
📄 23400-A	PREPARE/SUBMIT - HVAC DUCTWORK	40	29-Mar-24 08:00 A	30-Apr-24 17:00 A			📄	PREPARE/SUBMIT - HVAC DUCTWORK									
📄 23500-A	PREPARE/SUBMIT - HVAC EQUIPMENT - AHU/RTU/FANS/HEATERS/VFD's	40	29-Mar-24 08:00 A	01-Jul-24 17:00 A			📄	PREPARE/SUBMIT - HVAC EQUIPMENT - AHU/RTU/FANS/HEATERS/VFD's									
📄 23900-A	PREPARE/SUBMIT - HVAC DIFFUSERS/REGISTERS/GRILLES	60	29-Mar-24 08:00 A	24-Apr-24 17:00 A			📄	PREPARE/SUBMIT - HVAC DIFFUSERS/REGISTERS/GRILLES									
📄 26100-A	PREPARE/SUBMIT - ELECTRICAL MATERIALS - GEN SET	75	29-Mar-24 08:00 A	28-Jun-24 17:00 A			📄	PREPARE/SUBMIT - ELECTRICAL MATERIALS - GEN SET									
📄 26400-A	PREPARE/SUBMIT - PANELBOARDS	75	29-Mar-24 08:00 A	01-Jul-24 17:00 A			📄	PREPARE/SUBMIT - PANELBOARDS									
📄 26440-A	PREPARE/SUBMIT - SWITCHGEAR	70	29-Mar-24 08:00 A	01-Jul-24 17:00 A			📄	PREPARE/SUBMIT - SWITCHGEAR									
📄 26500-A	PREPARE/SUBMIT - ELECTRICAL FIXTURES - LIGHT FIXTURES	75	29-Mar-24 08:00 A	10-May-24 17:00 A			📄	PREPARE/SUBMIT - ELECTRICAL FIXTURES - LIGHT FIXTURES									
📄 27100-A	PREPARE/SUBMIT - COMMUNICATIONS	75	29-Mar-24 08:00 A	21-Jun-24 17:00 A			📄	PREPARE/SUBMIT - COMMUNICATIONS									
📄 28100-A	PREPARE/SUBMIT - FIRE ALARM SYSTEM	75	29-Mar-24 08:00 A	25-Jun-24 17:00 A			📄	PREPARE/SUBMIT - FIRE ALARM SYSTEM									
📄 26101-A	PREPARE/SUBMIT - ELECTRICAL MATERIALS - ATS	30	29-Mar-24 08:00 A	09-Jul-24 17:00 A			📄	PREPARE/SUBMIT - ELECTRICAL MATERIALS - ATS									


26-Aug-24 16:44

 Actual Level of Effort
 Remaining Work
 ◆ ◆ Milestone
 Actual Work
  Critical Remaining Work
 ▼ summary

26-Aug-24 16:44

	09310-B	REVIEW/APPROVE - TILING	10	04-Dec-24 08:00	17-Dec-24 17:00	102
	09510-B	REVIEW/APPROVE - ACOUSTICAL CEILINGS	10	04-Dec-24 08:00	17-Dec-24 17:00	99
	12310-B	REVIEW/APPROVE - CASEWORK - DIV. 12	10	04-Dec-24 08:00	17-Dec-24 17:00	97
	10140-B	REVIEW/APPROVE - SIGNAGE - GRAPHICS	10	18-Dec-24 08:00	02-Jan-25 17:00	97
	12240-B	REVIEW/APPROVE - WINDOW SHADES	10	18-Dec-24 08:00	02-Jan-25 17:00	107
	09640-B	REVIEW/APPROVE - WOOD ATHLETIC FLOORING	10	31-Dec-24 08:00	14-Jan-25 17:00	89
	FAB/DELIVER		345	29-Apr-24 08:00 A	23-Sep-25 17:00	11
	08800-C	FAB/DELIVER - GLAZING	70	29-Apr-24 08:00 A	03-Dec-24 17:00	150
	14210-C	FAB/DELIVER - ELEVATORS	80	02-May-24 08:00 A	17-Dec-24 17:00	136
	03300-C	FAB/DELIVER - REBAR SHOP DRAWINGS/CONC. MIX DESIGNS / AB's	55	03-May-24 08:00 A	16-May-24 17:00 A	
	23900-C	FAB/DELIVER - HVAC DIFFUSERS/REGISTERS/GRILLES	40	08-May-24 08:00 A	21-Oct-24 17:00	184
	23400-C	FAB/DELIVER - HVAC DUCTWORK	30	13-May-24 08:00 A	07-Oct-24 17:00	120
	07210-C	FAB/DELIVER - INSULATION - MINERAL WOOL	25	20-May-24 08:00 A	30-Sep-24 17:00	165
	07420-C	FAB/DELIVER - METAL WALL PANELS	50	20-May-24 08:00 A	04-Nov-24 17:00	211
	12480-C	FAB/DELIVER - ENTRANCE FLOOR MATS & FRAMES	70	24-May-24 08:00 A	03-Dec-24 17:00	172
	07840-C	FAB/DELIVER - FIREPROOFING	25	28-May-24 08:00 A	02-Aug-24 17:00 A	
	08100-C	FAB/DELIVER - HOLLOW METAL FRAMES	60	04-Jun-24 08:00 A	18-Nov-24 17:00	123
	10280-C	FAB/DELIVER - TOILET/BATH ACCESSORIES	50	04-Jun-24 08:00 A	04-Nov-24 17:00	211
	10220-C	FAB/DELIVER - FOLDING PANEL PARTITIONS	50	05-Jun-24 08:00 A	04-Nov-24 17:00	169
	10210-C	FAB/DELIVER - TOILET COMPARTMENTS	50	14-Jun-24 08:00 A	04-Nov-24 17:00	204
	07500-C	FAB/DELIVER - ROOFING	40	18-Jun-24 08:00 A	21-Oct-24 17:00	22
	08710-C	FAB/DELIVER - HARDWARE	60	26-Jun-24 08:00 A	18-Nov-24 17:00	199
	09650-C	FAB/DELIVER - FLOORING - CARPET	60	28-Jun-24 08:00 A	18-Nov-24 17:00	192
	04200-C	FAB/DELIVER - MASONRY - EXT. BRICK SAMPLES	35	01-Jul-24 08:00 A	14-Oct-24 17:00	110
	05120-C	FAB/DELIVER - STRUCTURAL STEEL FRAMING - SEQUENCES	55	01-Jul-24 08:00 A	17-Sep-24 17:00	13
	08200-C	FAB/DELIVER - DOORS	60	01-Jul-24 08:00 A	18-Nov-24 17:00	189
	22100-C	FAB/DELIVER - PLUMBING MATERIALS + ACCESSORIES	20	03-Jul-24 08:00 A	26-Aug-24 17:00	72
	08430-C	FAB/DELIVER - STOREFRONT/CURTAINWALLS	80	16-Jul-24 08:00 A	17-Dec-24 17:00	191
	08510-C	FAB/DELIVER - WINDOWS	80	16-Jul-24 08:00 A	17-Dec-24 17:00	191
	11400-C	FAB/DELIVER - FOOD SERVICE EQUIPMENT	80	16-Jul-24 08:00 A	17-Dec-24 17:00	182
	23500-C	FAB/DELIVER - HVAC EQUIPMENT - AHU/RTU/FANS/HEATERS/VFD's	50	17-Jul-24 08:00 A	04-Nov-24 17:00	144
	27100-C	FAB/DELIVER - COMMUNICATIONS	50	17-Jul-24 08:00 A	04-Nov-24 17:00	121
	21310-C	FAB/DELIVER - FIRE SPRINKLER SYSTEM + EQUIPMENT	50	18-Jul-24 08:00 A	04-Nov-24 17:00	154
	26100-C	FAB/DELIVER - ELECTRICAL MATERIALS - GEN SET	275	24-Jul-24 08:00 A	23-Sep-25 17:00	6
	26101-C	FAB/DELIVER - ELECTRICAL MATERIALS - ATS	107	24-Jul-24 08:00 A	24-Oct-24 17:00	216
	26114-C	FAB/DELIVER - GENERATOR	262	25-Jul-24 08:00 A	20-May-25 17:00	93
	26440-C	FAB/DELIVER - SWITCHGEAR	250	02-Aug-24 08:00 A		

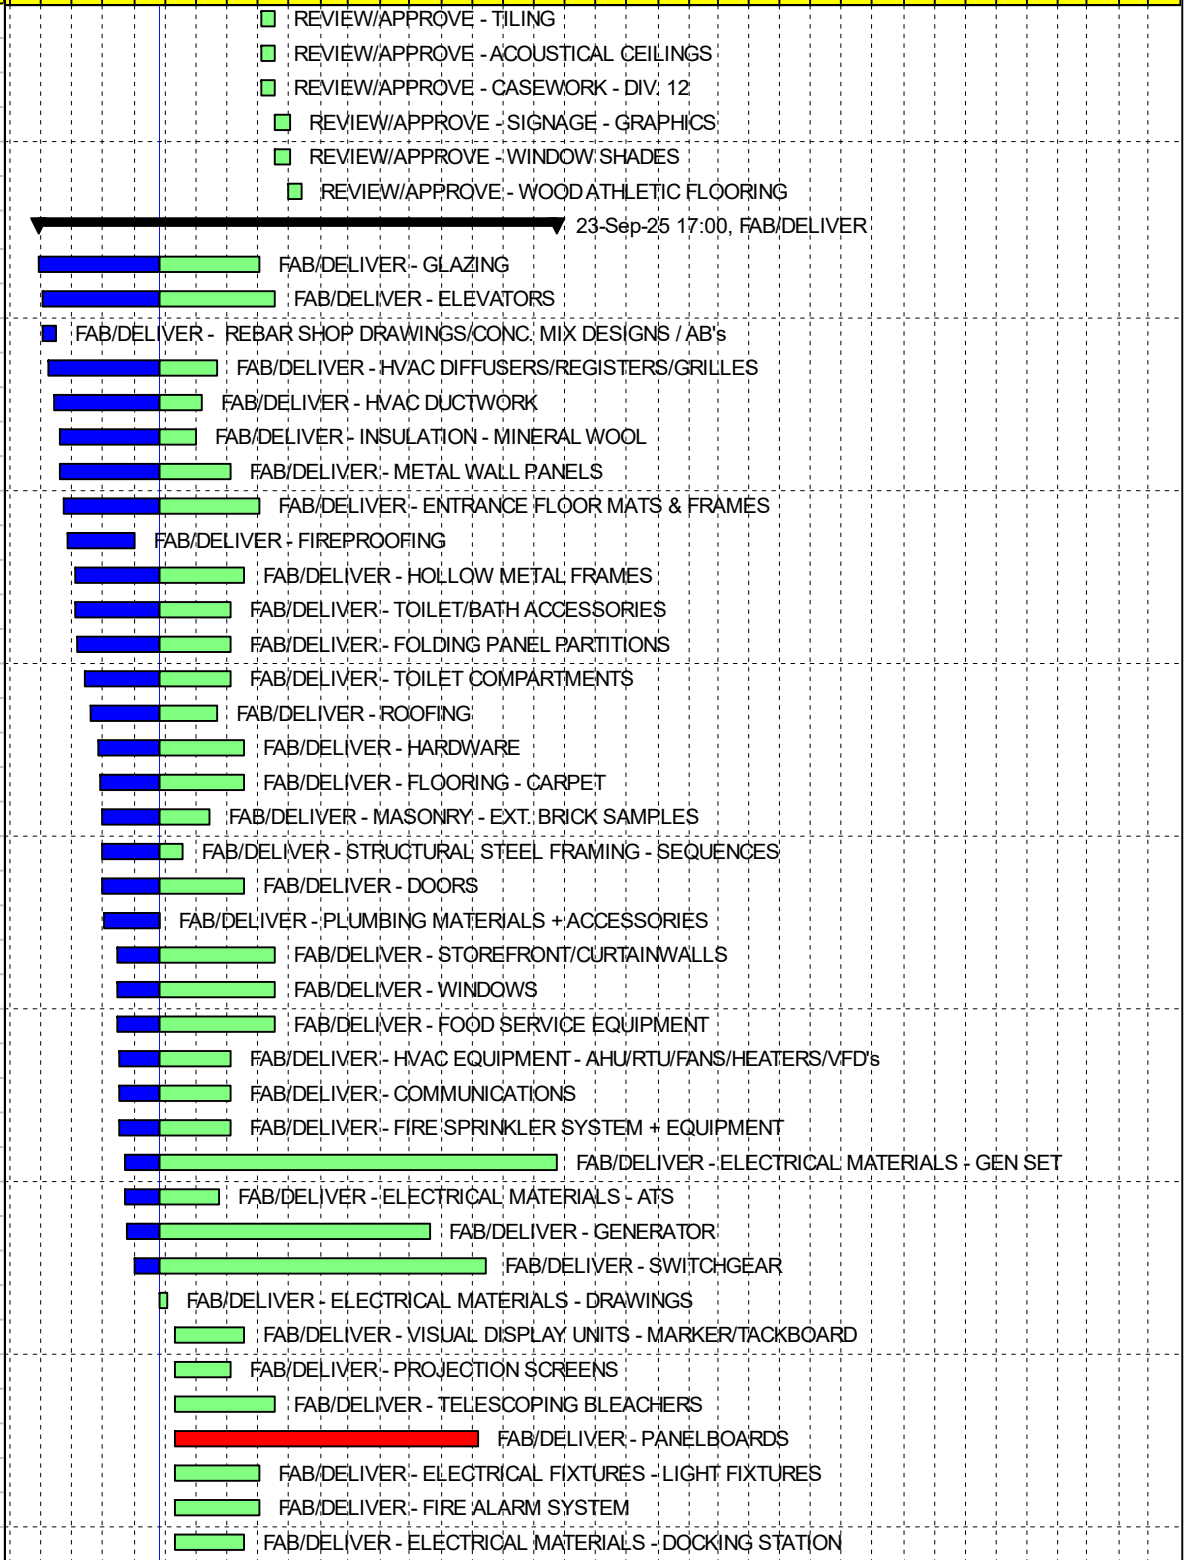

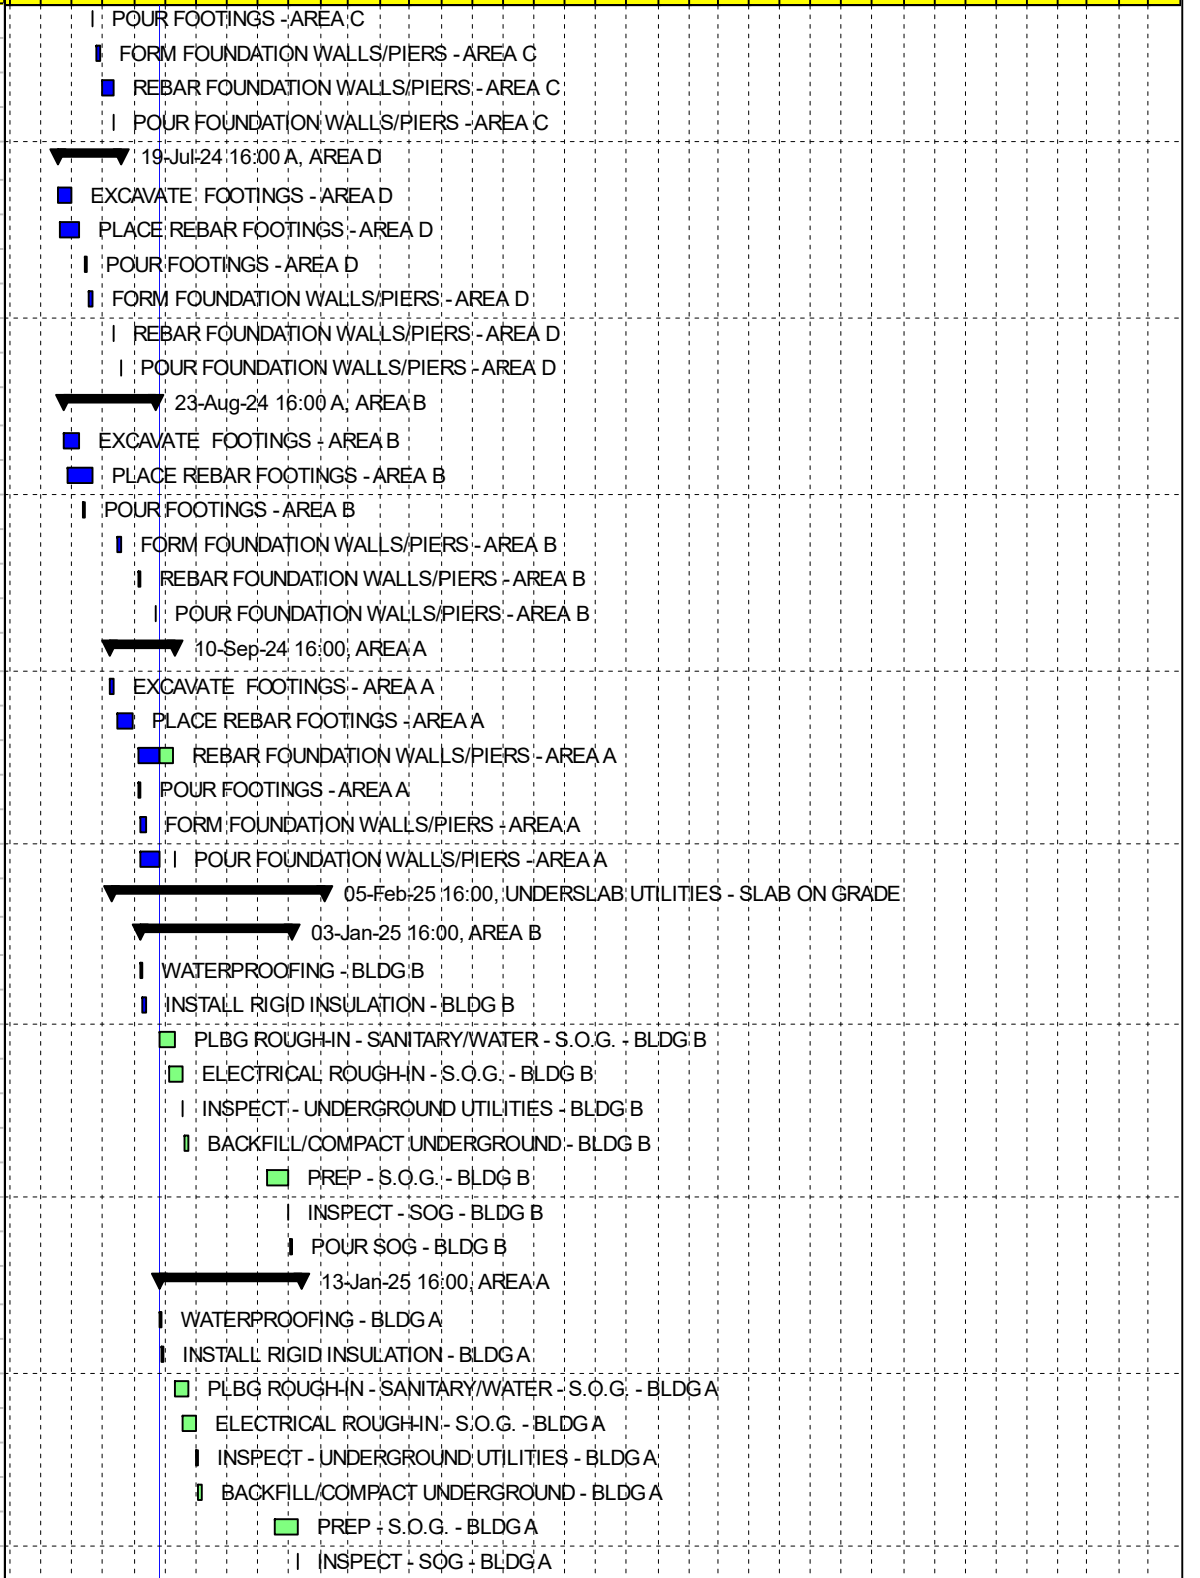[illegible]

 Actual Level of Effort
 Remaining Work
 Milestone
 Actual Work
  Critical Remaining Work
  summary

26-Aug-24 16:44

 Actual Level of Effort
  Remaining Work
 ◆ ◆ Milestone
 Actual Work
 Critical Remaining Work
 ▼ summary

26-Aug-24 16:44

 Actual Level of Effort
 Remaining Work
 Milestone

 Actual Work
  Critical Remaining Work
 summary

26-Aug-24 16:44

 Actual Level of Effort
 Remaining Work
 ◆ ◆ Milestone

 Actual Work
  Critical Remaining Work
 ▾ summary

LEVEL 2

26-Aug-24 16:44

 Actual Level of Effort
  Remaining Work
   Milestone

 Actual Work
  Critical Remaining Work
  summary

26-Aug-24 16:44

 Actual Level of Effort
  Remaining Work
  Milestone

 Actual Work
 Critical Remaining Work
 summary

[illegible]

26-Aug-24 16:44

© Oracle Corporation

26-Aug-24 16:44

 Actual Level of Effort
 Remaining Work
 Milestone

 Actual Work
  Critical Remaining Work
  summary

26-Aug-24 16:44

 Actual Level of Effort
 Remaining Work
 Milestone
 Actual Work
  Critical Remaining Work
  summary

26-Aug-24 16:44

 Actual Level of Effort
  Remaining Work
   Milestone

 Actual Work
  Critical Remaining Work
  summary

26-Aug-24 16:44

 Actual Level of Effort
  Remaining Work
   Milestone

 Actual Work
  Critical Remaining Work
  summary

[illegible]

26-Aug-24 16:44

 Actual Level of Effort
  Remaining Work
 ◆ ◆ Milestone
 Actual Work
 Critical Remaining Work
 ▼ summary

